

# Kansas Corporation Commission

## Abandoned Well Plugging Federal Program

### Initial Grant Project Proposal


Project awards are subject to the Kansas Corporation Commission receiving orphaned well plugging funds pursuant to the Bipartisan Infrastructure Law (IIJA) Section 40601.

The number of wells in a project may change as wells are added or removed from the project and may continue to change until the project is complete. Information is updated quarterly by county in the tables below.

#### Federal Initial Grant Project Proposal

## Federal Initial Grant Projects

### Overview

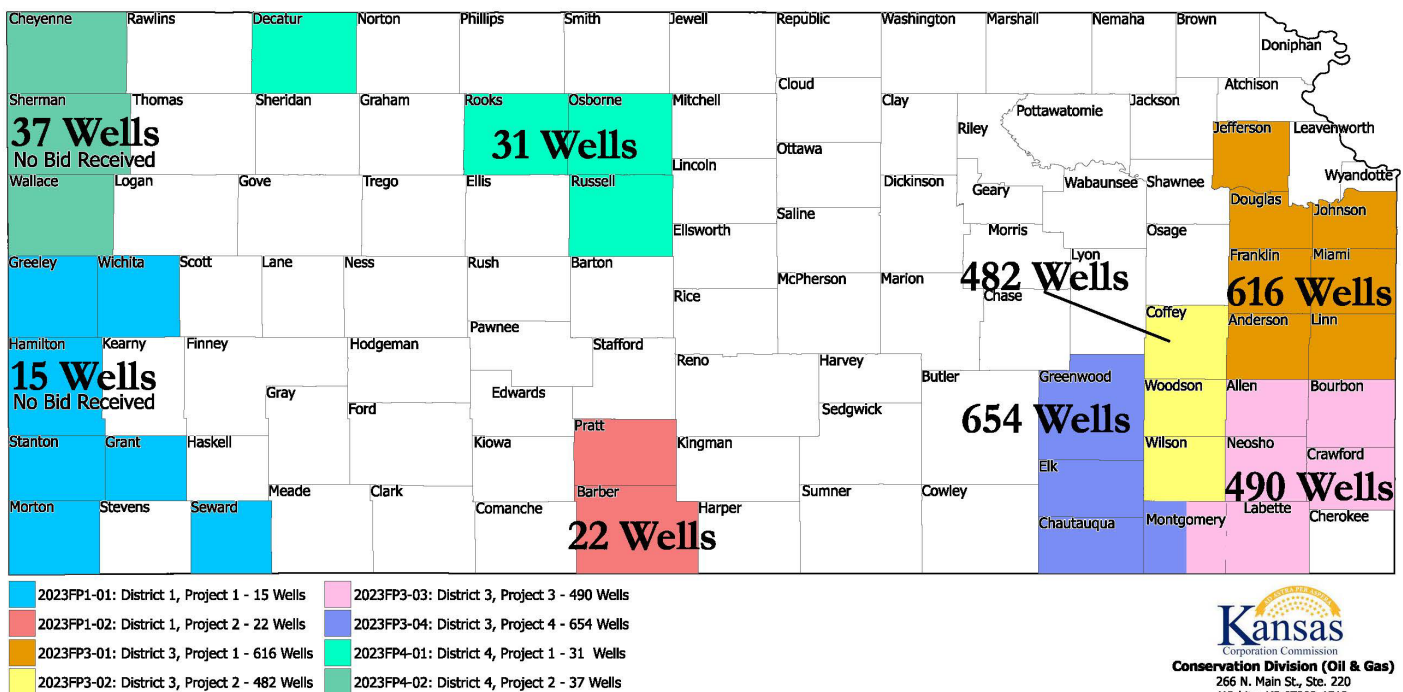

District 1 – Project 1 (2023FP1-01) = 15 wells  
District 1 – Project 2 (2023FP1-02) = 22 wells


District 3 – Project 1 (2023FP3-01) = 616 wells  
District 3 – Project 2 (2023FP3-02) = 482 wells  
District 3 – Project 3 (2023FP3-03) = 490 wells  
District 3 – Project 4 (2023FP3-04) = 654 wells

District 4 – Project 1 (2023FP4-01) = 31 wells  
District 4 – Project 2 (2023FP4-02) = 37 wells

# Federal Initial Grant Projects

## Wells Plugged

1/16/2023 - 3/31/2023

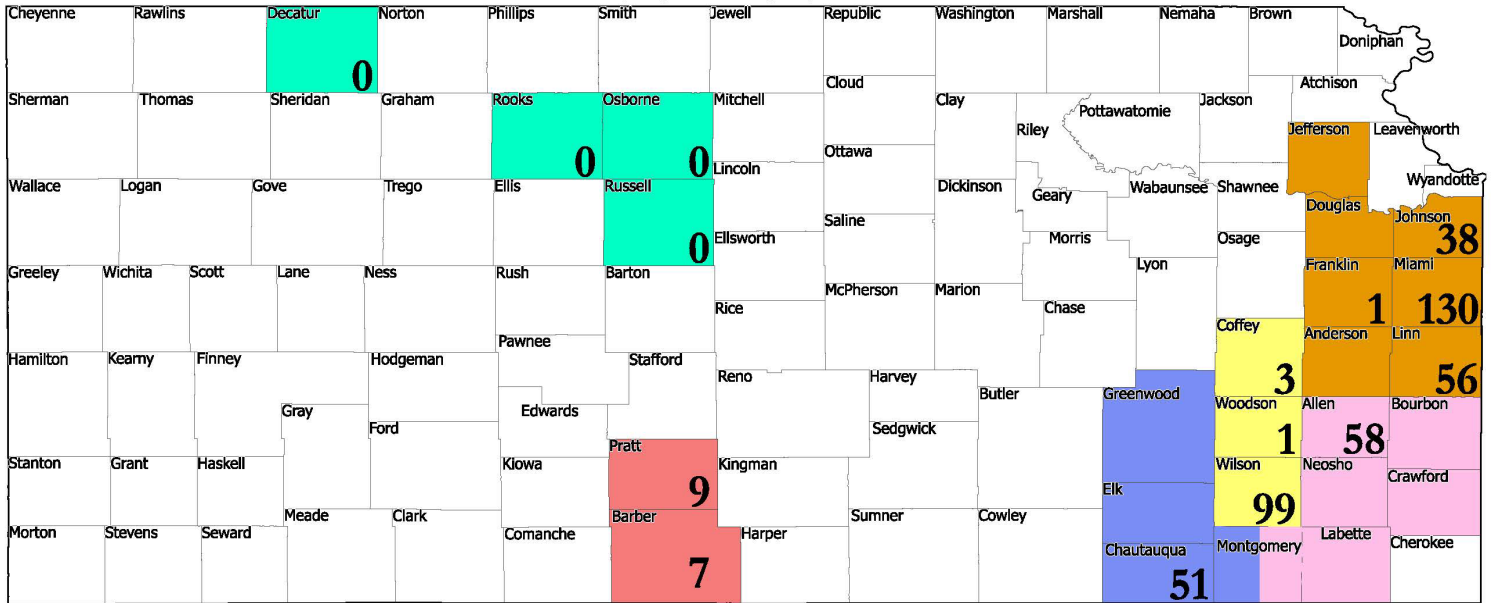

2023FP1-02: District 1, Project 2 - 22 Wells  
 2023FP3-01: District 3, Project 1 - 616 Wells  
 2023FP3-02: District 3, Project 2 - 482 Wells  
 2023FP3-03: District 3, Project 3 - 490 Wells  
 2023FP3-04: District 3, Project 4 - 654 Wells  
 2023FP4-01: District 4, Project 1 - 31 Wells

State-wide total of wells plugged to-date: 453

Map indicates the number of wells plugged in each county using federal funding from the initial grant. Number in legend indicates the total number of wells in each project.

**Kansas**  
 Corporation Commission  
**Conservation Division (Oil & Gas)**  
 266 N. Main St., Ste. 220  
 Wichita, KS 67202-1513  
 Phone: (316) 337-6200  
 Fax: (316) 337-6211

Well information update as of 03.31.2023

State of Kansas Abandoned Well Plugging • Federal Program	
Federal Initial Grant	
Initial Funds Available TOTAL	\$25,000,000.00
<b>INITIAL ESTIMATED AMOUNTS</b>	
Initial Estimated TOTAL Wells	2165
Initial Estimated TOTAL Projects Cost	\$24,862,078.74
<b>WELLS PLUGGED (as of 03.31.2023)</b>	
TOTAL Wells	453
TOTAL Cost	\$5,067,496.56
<b>INVOICED (PAID) AMOUNTS (as of 03.31.2023)</b>	
TOTAL Invoiced (Paid) Wells	380
TOTAL Invoiced (Paid) Project Cost	\$3,856,686.64

District 1 – Project 2 Wells			
<i>COUNTY</i>	<i>INITIAL ESTIMATE</i>	<i>PLUGGED As of 03.31.2023</i>	<i>INVOICED (PAID) As of 03.31.2023</i>
Barber	7	7	4
Pratt	15	9	0
<b>TOTAL Wells</b>	<b>22</b>	<b>16</b>	<b>4</b>
<b>TOTAL Project Cost</b>	<b>\$1,626,778.74</b>	<b>\$477,146.56</b>	<b>\$119,286.64</b>

\* Project plugging costs only reflect 4 of the 16 wells plugged. Plugged Price is estimated.

District 4 – Project 1 Wells			
<i>COUNTY</i>	<i>INITIAL ESTIMATE</i>	<i>PLUGGED As of 03.31.2023</i>	<i>INVOICED (PAID) As of 03.31.2023</i>
Decatur	8	0	0
Rooks	8	0	0
Osborne	3	0	0
Russell	12	0	0
<b>TOTAL Wells</b>	<b>31</b>	<b>0</b>	<b>0</b>
<b>TOTAL Project Cost</b>	<b>\$1,992,400.00</b>	<b>\$0.00</b>	<b>\$0.00</b>

\* No wells have been plugged or completed.

District 3 – Project 1 Wells			
<i>COUNTY</i>	<i>INITIAL ESTIMATE</i>	<i>PLUGGED As of 03.31.2023</i>	<i>INVOICED (PAID) As of 03.31.2023</i>
Anderson	47	0	0
Douglas	67	0	0
Franklin	20	1	0
Jefferson	11	0	0
Johnson	84	38	38
Linn	206	56	56
Miami	181	130	123
<b>TOTAL Wells</b>	<b>616</b>	<b>225</b>	<b>217</b>
<b>TOTAL Project Cost</b>	<b>\$6,160,000.00</b>	<b>\$2,250,000.00</b>	<b>\$2,170,000.00</b>

District 3 – Project 2 Wells			
<i>COUNTY</i>	<i>INITIAL ESTIMATE</i>	<i>PLUGGED As of 03.31.2023</i>	<i>INVOICED (PAID) As of 03.31.2023</i>
Coffey	157	3	0
Wilson	243	99	91
Woodson	82	1	1
<b>TOTAL Wells</b>	<b>482</b>	<b>103</b>	<b>92</b>
<b>TOTAL Project Cost</b>	<b>\$5,277,900.00</b>	<b>\$1,127,850.00</b>	<b>\$1,007,400.00</b>

District 3 – Project 3 Wells			
<i>COUNTY</i>	<i>INITIAL ESTIMATE</i>	<i>PLUGGED As of 03.31.2023</i>	<i>INVOICED (PAID) As of 03.31.2023</i>
Allen	107	58	23
Bourbon	4	0	0
Crawford	70	0	0
Labette	87	0	0
Montgomery	82	0	0
Neosho	140	0	0
<b>TOTAL Wells</b>	<b>490</b>	<b>58</b>	<b>23</b>
<b>TOTAL Project Cost</b>	<b>\$4,900,000.00</b>	<b>\$580,000.00</b>	<b>\$230,000.00</b>

District 3 – Project 4 Wells			
<i>COUNTY</i>	<i>INITIAL ESTIMATE</i>	<i>PLUGGED As of 03.31.2023</i>	<i>INVOICED (PAID) As of 03.31.2023</i>
Chautauqua	172	51	44
Elk	24	0	0
Greenwood	175	0	0
Montgomery	107	0	0
Neosho	176	0	0
<b>TOTAL Wells</b>	<b>654</b>	<b>51</b>	<b>44</b>
<b>TOTAL Project Cost</b>	<b>\$4,905,000.00</b>	<b>\$382,500.00</b>	<b>\$330,000.00</b>
